ID	Task Name
1	**CALICE WP2 - M. Wing (UCL)**
2	**Readout of prototype VFE ASICs**
3	Firmware development for multi-chip tests
4	Multichip tests
5	**Study of data paths over 1.5m slab**
6	Preliminary design study and preparation
7	Test Panel 0 design, fabrication and commissioning
8	FE board 0 design, fabrication and commissioning
9	Test bench 0 hardware ready and commissioned
10	Test bench 0 + host PC tests and measurements
11	Results analysis concepts definition for phase 1
12	Concepts established for 1.5m data path
13	Test panel 1 design and fabrication
14	Test bench 1 hardware ready and complete
15	Test panel 1 measurement programme
16	Test panel 1 complete
17	Define DIF-LDA protocol
18	DIF hardware design, fabrication and commissioning
19	DIF firmware - minimal version
20	DIF completed
21	Intermediate board hardware and commissioning
22	DIF firmware - final version
23	ECAL DIF available for test beams
24	System integration
25	**DAQ Networking**
26	FPGA to 1 Gig ethernet firmware development
27	FPGA 1 Gig Ethernet MAC firmware complete
28	1Gb data transfer tests
29	1Gb FPGA to multiple destination network tests
30	Report on FPGA ethernet work
31	Generic data source development
32	Re-package generic input data as ethernet
33	Multi-port gigabit firmware development
34	Multi-port gigabit network tests
35	10Gb hardware development
36	10Gb tests
37	Network integration with electronics
38	Report on 10Gb performance
39	Networking tests with FPGA data source
40	Survey of optical switches available
41	Acquire optical switch
42	Build network test rig using optical switch
43	Evaluate network performance
44	Re-evaluate performance with switching
45	Demonstrate optically switched network
46	Build busy signal
47	Develop trigger interface

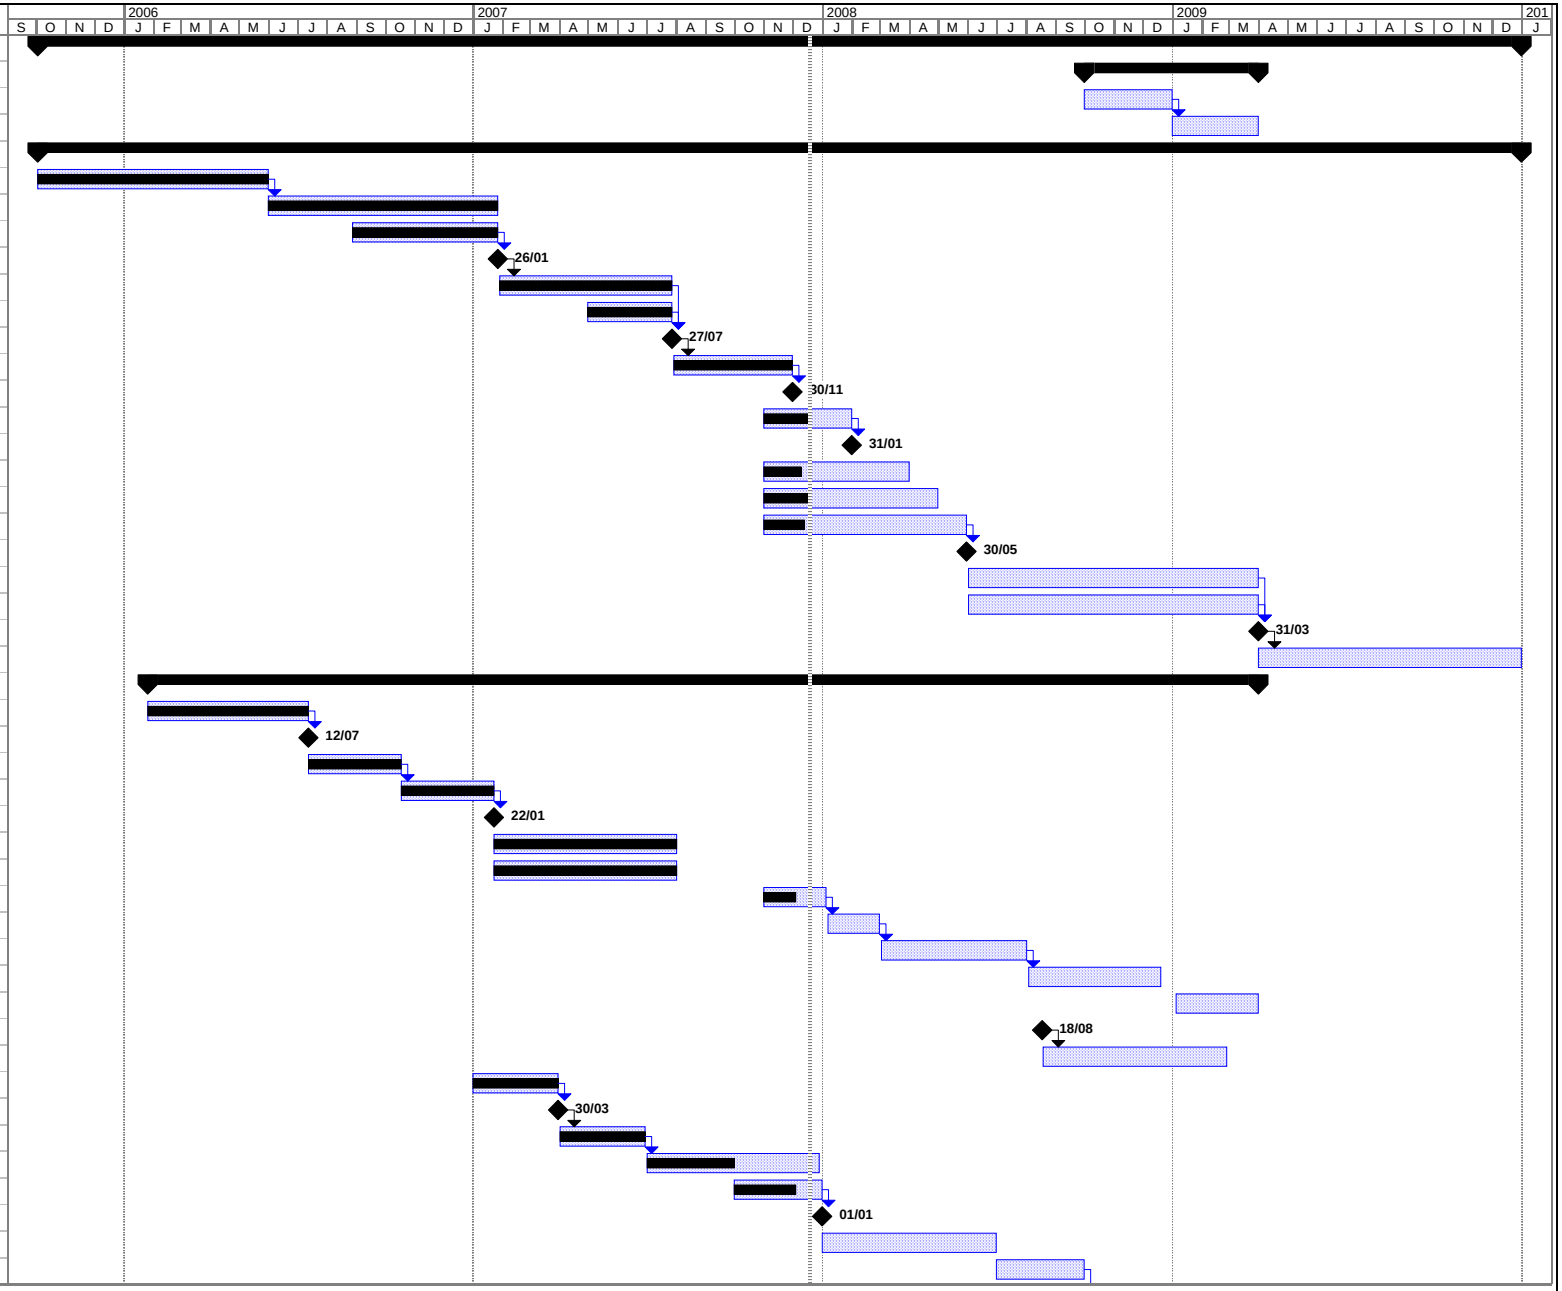

Project: WP2
Date: Tue 18/12/07

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name
48	Develop automatic switching system
49	Delivery of busy system
50	LDA low-level firmware development
51	LDA-DIF link operational at electrical level
52	LDA high-level firmware and integration
53	Working LDA with C&C and ODR
54	System integration
55	**Transport of configuration, clock and control data**
56	Simulate radiation environment at FE
57	Present simulation results
58	Literature search for expected problems
59	Design prototype board and test system
60	Make proposal for robust/flexible test system
61	Define clock and trigger requirements
62	Design/prototype lock extraction system
63	Evaluate use of commercial hardware fanout
64	Demonstrate trigger (and C + C) fanout
65	Design required interfaces
66	Demonstrate system lock from data interface
67	Evaluate jitter
68	Build large system
69	Demonstrate workability from single trigger source
70	Design remote configuration hardware
71	Expand hardware to multiple units
72	Demonstrate remote FGPA reset and reconfigure
73	**Prototype off-detector receiver**
74	Investigated latest PCI technology
75	Buy PCI cards
76	High level system design
77	Produce prototype firmware
78	Write system software
79	Initial prototype complete
80	Tests of initial prototype
81	Enhancements - s/w to h/w for speed improvements
82	Enhancements - data to pseudo-file format
83	Initial system complete
84	Tests of initial system
85	Build and test full-scale system
86	Integrate into EUDET tets module
87	**DAQ software**
88	Define overall DAQ structure
89	DAQ software choice
90	Interface to hardware
91	Software and run control development
92	Complete basic DAQ and run control
93	System integration
94	Test beam support

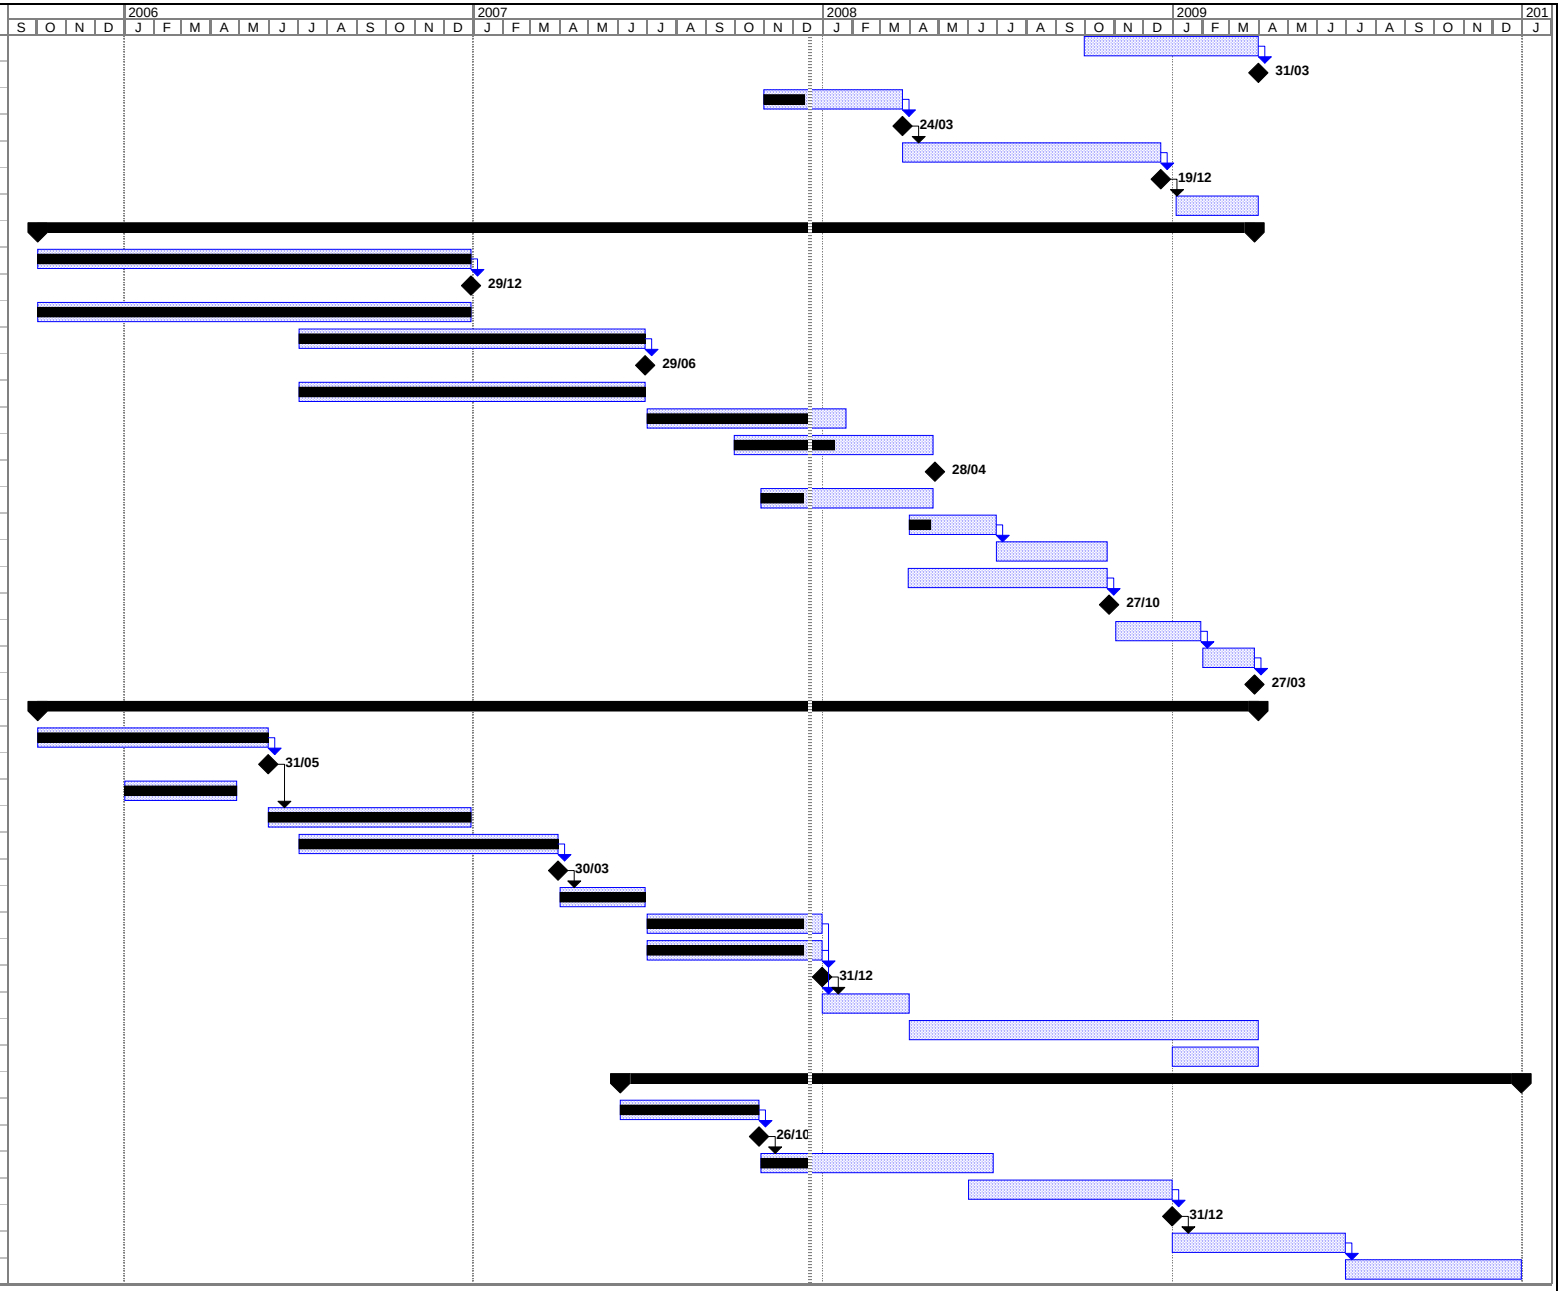

Project: WP2
Date: Tue 18/12/07

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
